


RMS Interfaces



May 2010

RMS Center - Apple Valley, CA



RMS Interface - Outline

- **RMS-CRMS-P2 Interface**
- **RMS-CEFMS Interface**
- **RMS-CCASS Interface**
- **RMS-SPS (PD2) Interface**



RMS Relationships to Other Systems

- **RMS-CRMS-P2**

- RMS provides Construction Status Information

- RMS feeds Headquarters information via P2

- **RMS-CEFMS**

- RMS downloads funding information from CEFMS

- RMS uploads progress payments to CEFMS

- **RMS-CCASS**

- The evaluation will be exported from RMS to CCASS

- CCASS will provide updated status to RMS thru completion

- **RMS-PD2 (SPS)**

- RMS will communicate contract modifications w/SPS via a sometime-to-be-released RMS-SPS interface



RMS-CRMS-P2 Interface

- **Modifications/Proposed Changes**
- **Feature of Work Schedule**
- **Scheduled/Actual Progress**
- **Major Milestone Events**
- **Construction/Customer Issues**

Financial Tree



This is where the money and appropriation data comes from.


Finances 101

This shows the Authorized amount for this Contract(s).

These are used to link expenses (gives us the structure).

Obligates funds for Payment (ENG Form 93)

Commitment of Funds (Reduces available \$\$\$)

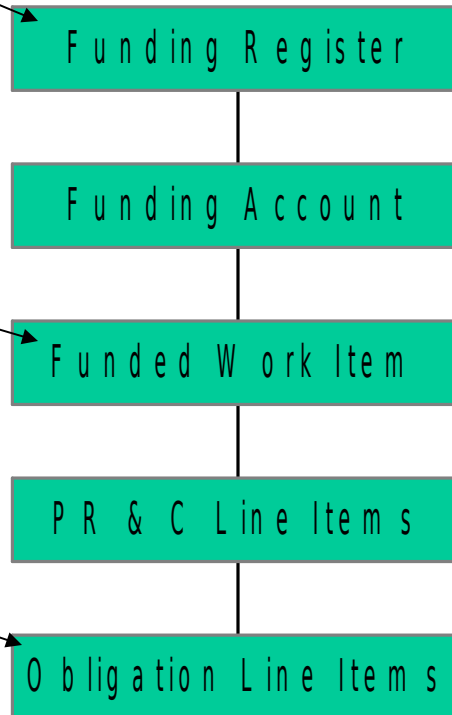



Modifications/Proposed Changes

- **Award Contract Amount**
- **Signed Modifications**
- **Funded Pending Changes**
- **Unfunded Pending Changes**

RMS computes contingency by subtracting pending changes from available funding in CEFMS



Feature of Work Schedule

- **Contractor schedules construction by work activities (100's to 1,000's)**
- **Actives are grouped by Definable Features of Work (10 to 30)**
- **RMS sends P2 scheduled & actual start and finish dates of each feature**


McGraw-Hill Controls Contractor's NAS up to a feature schedule



Major Milestone Events

- **Contract Award from P2**
- **Notice to Proceed (NTP) Acknowledged**
- **Beneficial Occupancy Date (BOD)**
- **Construction Completion**
- **Physical Completion**
- **Construction Start Date**
- **Fiscal Completion (Final Payment)**

Scheduled vs. Actual Construction

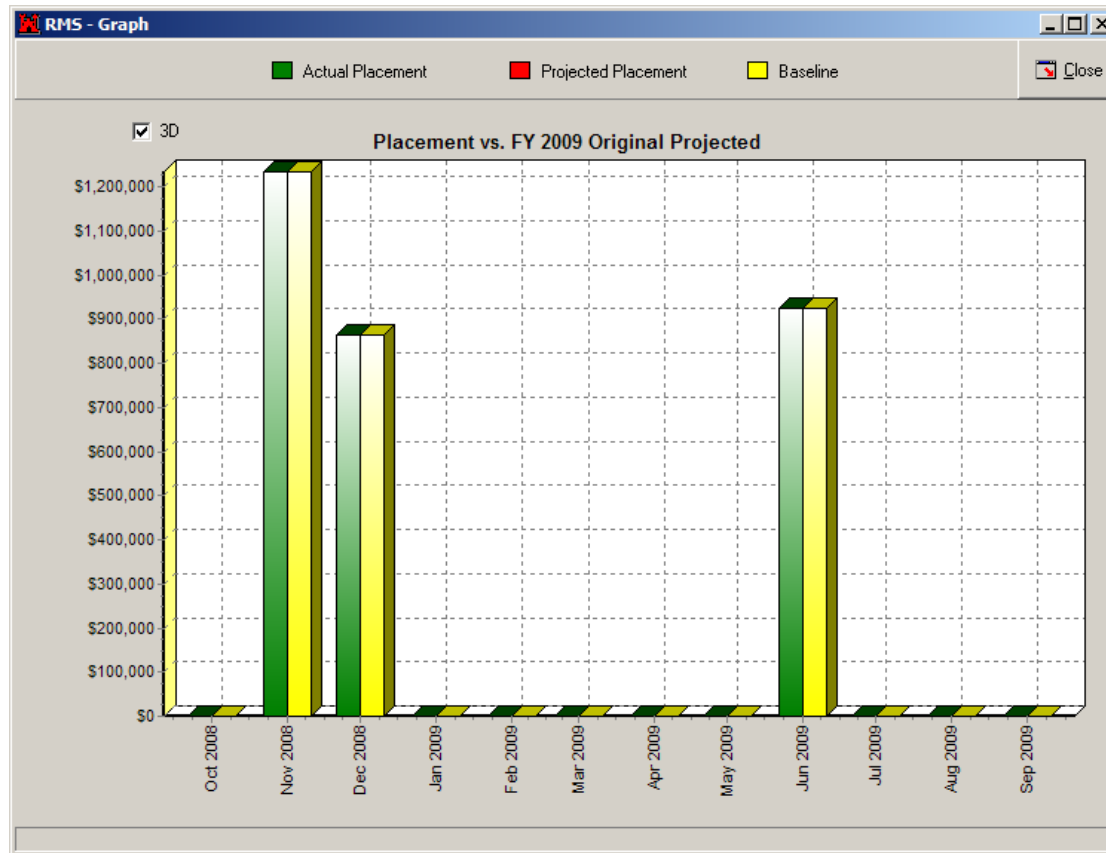

**RMS-CRMS sends P2
Scheduled and Actual Construction Progress**



Customer/ Construction Issues

- **Narrative on Customer Issues**
- **Narrative on USACE Issues**
- **Construction Status Code**
- **Primary Delay Code**



Questions?
